

Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates
September 2026

Neabsco-Potomac Commuter Parking Garage

Project #16C17004

***Federal, State, and Local Funding**
Woodbridge Magisterial District



Updates:

- Installation of landscaping, final grading of the stormwater management pond, and seeding to ensure proper germination is ongoing.
- **Construction has begun on a short segment of sidewalk in front of Sentara Hospital.**
- **Continuing project close-out on punch list items for VDOT acceptance.**

Issues:

- None

Timeline:

	Beginning	Ending	Changed from prior report?
Location Study:	March/April 2018 (FY18)	August 2018 (FY19)	N/A
Preliminary Design:	April 2019 (FY19)	April 2020 (FY20)	N/A
Right-of-Way:	N/A	N/A	N/A
Design-Build RFP Issuance	March 2020 (FY20)	September 2021 (FY22)	N/A
Design/Construction:	March 2022 (FY22)	Summer 2026 (FY26)	N/A

Budget:

\$54,672,000

**Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates**

**Devlin Road Widening
Project #21C17001
*State and Local Funding
Brentsville Magisterial District**



Updates:

- **Continued coordination with PWC Police to minimize impact on school traffic.**
- **Construction activities including mill and overlay work to expand the shoulder westbound on Devlin Road are ongoing.**

Issues:

- NOVEC is scheduled to remove an existing pole on Jennell Drive and Devlin Road.
- Comcast utility relocation is currently ongoing on the eastbound side of Devlin Road.
- A coordinated effort to resolve issues of multiple conduit interferences with proposed work with Verizon, Summit IG, and Comcast.

Timeline:

	Beginning	Ending	Changed from prior report?
Design:	November 2020 (FY21)	July 2024 (FY25)	N/A
Right-of-Way:	Winter 2022 (FY22)	January 2024 (FY24)	N/A
Construction Bidding:	June 2025 (FY25)	August 2025 (FY26)	N/A
Construction:	December 2025 (FY26)	Spring 2028 (FY28)	N/A

Budget:

\$74,316,830

**Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates**

University Boulevard Extension (Devlin Road to Wellington Road)

Project #23C17023

***Federal, State, and Regional
Brentsville Magisterial District**



Updates:

- **Project will go before the Commonwealth Transportation Board (CTB) in October 2026 for approval.**
- **Initial financial plan was submitted to VDOT for review.**
- **NEPA approval review continues.**

Issues:

- Current project estimate exceeds the funds available.
- Pursuing SmartScale funding and calling in proffered Right-of-Way to cover the deficit.

Timeline:

	Beginning	Ending	Changed from prior report?
Preliminary Design	April 2023 (FY23)	Summer 2025 (FY26)	N/A
Right-of-Way	N/A	N/A	N/A
Design-Build RFQ/RFP	Fall 2025 (FY26)	Spring 2027 (FY27)	N/A
Design-Build Contract Execution	Spring 2027 (FY27)	Winter 2028 (FY29)	N/A

Budget:

\$93,622,509

**Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates**

**Intersection Improvements at Prince William Parkway and University Boulevard
(Quadrant Roadway Intersection)**

Project #19C17004

***Regional and Local Funding
Brentsville Magisterial District**



Updates:

- **Minor punch list item (signage) is wrapping up, and VDOT acceptance is expected in September 2026.**

Issues:

- None

Timeline:

	Beginning	Ending	Changed from prior report?
Design:	December 2018 (FY19)	January 2022 (FY22)	N/A
Right-of-Way:	February 2020 (FY20)	September 2021 (FY22)	N/A
Construction Bidding:	February 2022 (FY22)	March 2022 (FY22)	N/A
Construction:	July 2022 (FY23)	December 2024 (FY25)	N/A

Budget:

\$31,713,000

Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates

Summit School Road and Telegraph Road

Project #19C17007

***Regional and Local Funding**
Occoquan Magisterial District



Updates:

- **Construction activities are ongoing.**

Issues:

- The construction contractor encountered several unmarked utility lines.
- Working with a property owner who installed a portion of their fence in the Right-of-Way.
- The contractor submitted a request for a time extension, which is currently under County review.

Timeline:

	Beginning	Ending	Changed from prior report?
Design:	December 2019 (FY20)	August 2021 (FY22)	N/A
Right-of-Way:	November 2020 (FY21)	April 2022 (FY22)	N/A
Construction Bidding:	March 2024 (FY24)	April 2024 (FY24)	N/A
Construction:	June 2024 (FY24)	Fall 2026 (FY27)	Yes

Budget:

\$39,969,468

**Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates**

Old Bridge Road-Occoquan Road Intersection

Project #20C17015

***Federal Funding**

Occoquan Magisterial District



Updates:

- Construction activities are ongoing, including installation of storm sewer structures, demolition of structures, and utility disconnect, and a pre-construction meeting with Prince William Water.
- **Construction activities are ongoing.**

Issues:

- None

Timeline:

	Beginning	Ending	Changed from prior report?
Design:	June 2020 (FY20)	Fall 2022 (FY23)	N/A
Right-of-Way:	Fall 2022 (FY23)	Spring 2024 (FY24)	N/A
Construction Bidding:	June 2025 (FY25)	July 2025 (FY26)	N/A
Construction:	Fall 2025 (FY26)	Summer 2027 (FY28)	N/A

Budget:

\$15,808,614


**Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates**

Van Buren Road Environmental Study and Design

Project #21C17004

***Local Funding**

Potomac Magisterial District

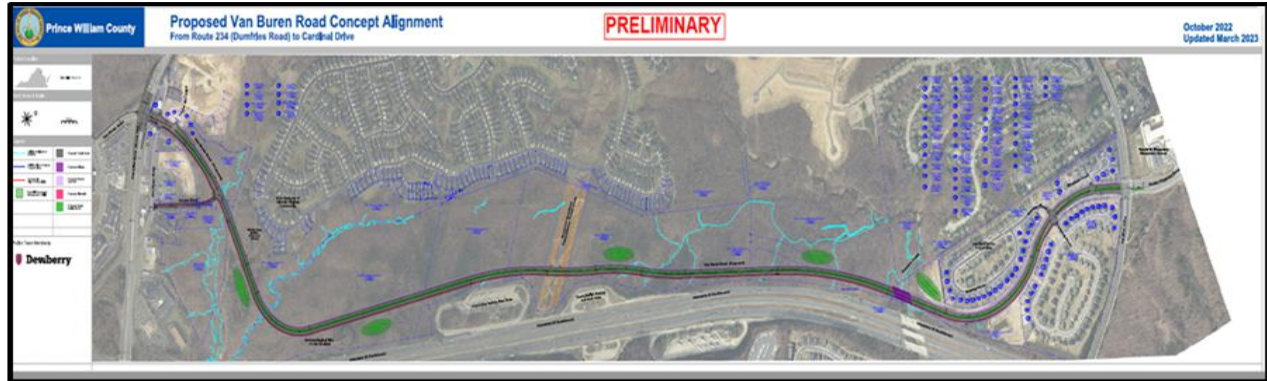

Updates:

- Value engineering reports/results are under consideration.
- Bridge designs continue.
- NVTa approved \$180M to fully fund the project in FY30.
- **Design activities are ongoing.**

Issues:

- None

Timeline:

	Beginning	Ending	Changed from prior report?
Study:	Summer 2020 (FY21)	Summer 2025 (FY26)	N/A
Design:	December 2024 (FY25)	Summer 2027 (FY28)	N/A
Right-of-Way:	TBD	TBD	N/A
Construction Bidding:	TBD	TBD	N/A
Construction:	TBD	TBD	N/A

Budget:

\$10,000,000


**Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates**

Fraleley Boulevard Widening: Route 1 (Brady's Hill Road to Route 234)

Project #21C17008

***Regional Funding**

Potomac Magisterial District

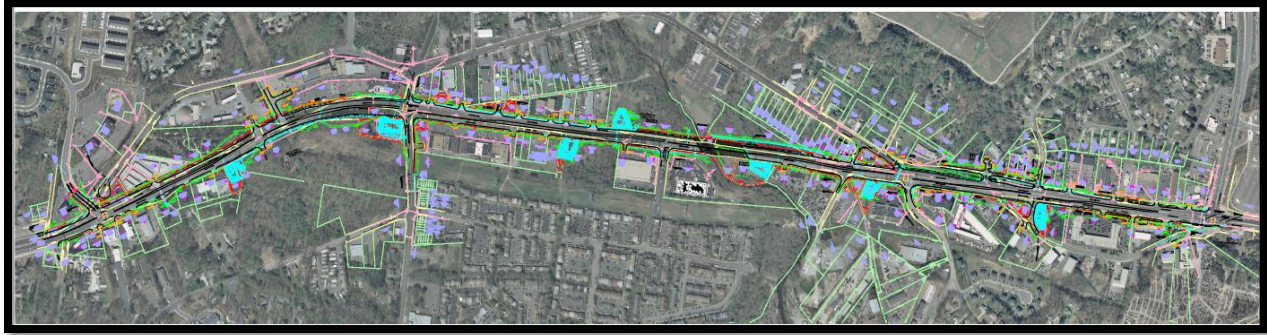

Updates:

- Coordination on environmental inspection and demolition of buildings before roadway construction is ongoing.
- The Town of Dumfries received federal funds for underground utilities within the project area. Dumfries will underground utilities separately from this roadway project.
- **Utility relocations continue.**

Issues:

- Securing permits and utility letters for demolition is ongoing.

Timeline:

	Beginning	Ending	Changed from prior report?
Design:	June 2021 (FY22)	Fall 2026 (FY27)	Yes
Right-of-Way:	September 2022 (FY23)	July 2026 (FY27)	Yes
Construction Bidding:	Winter 2027 (FY28)	Spring 2028 (FY28)	N/A
Construction:	Spring 2028 (FY28)	Winter 2031 (FY32)	N/A

Budget:

\$50,546,231

**Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates**

Minnieville Road-Prince William Parkway Interchange

Project #21C17002

***Local Funding**

Neabsco Magisterial District



Updates:

- **The County collaborated with consultants, contractors, and VDOT to revise the design plans and address VDOT structural and bridge review comments after a re-design was necessary. The revised plans have been approved.**
- **Beginning September 22nd, most left-turn movements at this intersection will be temporarily restricted to allow crews to continue construction. Through traffic and all right turns will remain open in every direction. The left turn from eastbound northbound Prince William Parkway to southbound westbound Minnieville Road will also remain open. PWC DTCC is coordination this effort with PWC Communications and Engagement, VDOT, GIS, Schools, Fire and Rescue, and the Police.**

Issues:

- The County is working with VDOT and contractors to submit temporary signal plans for approval and obtain temporary signal permits for construction. Schedule impact analysis submitted by the contractor is under review to determine if the change in the retaining walls justifies additional time or compensation.

Timeline:


	Beginning	Ending	Changed from prior report?
Design:	April 2022 (FY22)	May 2025 (FY25)	N/A
Right-of-Way:	January 2024 (FY24)	July 2025 (FY26)	N/A
Construction Bidding:	August 2025 (FY26)	October 2025 (FY26)	N/A
Construction:	March 2026 (FY26)	April 2028 (FY28)	N/A

Budget:

\$80,938,103

**Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates**

**Prince William Parkway and Clover Hill Road Interchange
Project #23C17005
*Regional Funding
Coles Magisterial District**

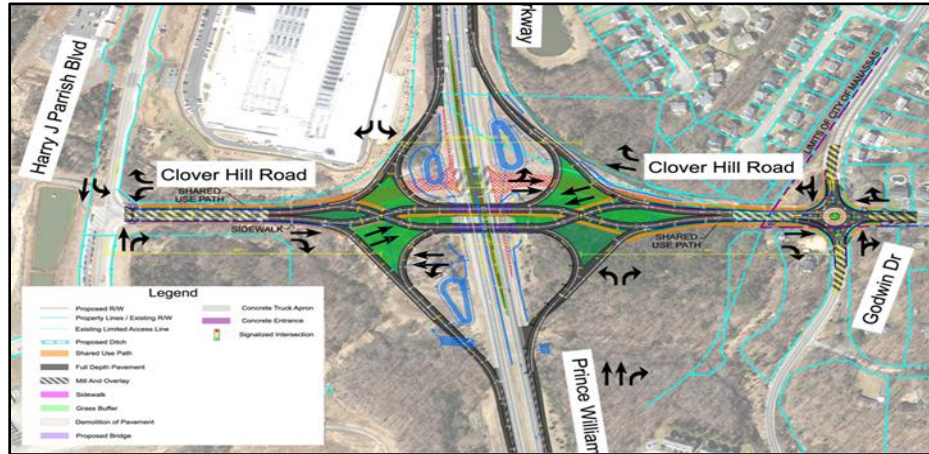

Updates:

- A well-attended Public Information Meeting was held on July 30, 2026, at the Washington Manassas Airport. Public comments period closed on August 12, 2026.
- **Addressing public information comments, including a FOIA request.**
- **An application for Smart Scale funding will be submitted.**
- **30% design plans are in progress.**

Issues:

- **The project is not fully funded.**

Timeline:

	Beginning	Ending	Changed from prior report?
Design:	February 2025 (FY25)	Winter 2026 (FY27)	N/A
Right-of-Way:	TBD	TBD	N/A
Construction Bidding:	TBD	TBD	N/A
Construction:	TBD	TBD	N/A

Budget:

\$3,040,000


**Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates**

Realignment of Prince William Parkway at Old Bridge Road

Project #22C17008

*** Federal Funding**

Occoquan Magisterial District

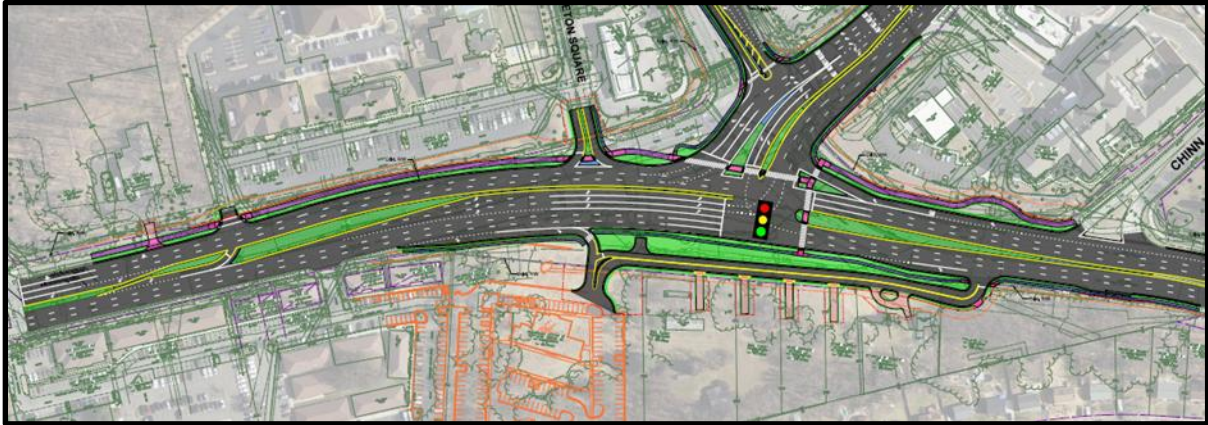

Updates:

- Coordination with utilities is ongoing. A Notice to Proceed was issued to Dominion Energy and DTCC is awaiting their response.
- Washington Gas relocation is underway.
- **All Right-of-Way is now cleared.**

Issues:

- None

Timeline:

	Beginning	Ending	Changed from prior report?
RFP:	March 2022 (FY22)	May 2022(FY22)	N/A
Design:	May 2022 (FY22)	Spring 2027 (FY27)	N/A
Right-of Way:	Summer 2025 (FY26)	Summer 2026 (FY27)	N/A
Construction Bidding:	Summer 2027 (FY28)	Summer 2027 (FY28)	N/A
Construction:	Summer 2027 (FY28)	Winter 2028 (FY29)	N/A

Budget:

\$35,487,806

**Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates**

**Marina Way Extension
Project #23C17011
* Federal Funding
Woodbridge Magisterial District**



Updates:

- Signal foundation design review comments were received from VDOT. The comments are being addressed. A second set of comments was received that are now being addressed.
- **VDOT authorized the contract award on August 25, 2026. PWC Procurement received a request to award the contract. DTCC is awaiting issuance of a Notice to Proceed for construction.**
- **Coordination began with PWC Public Works and VDOT to obtain a permit for construction.**

Issues:

- Design activities and construction schedule coordination with neighboring developers is ongoing.

Timeline:

	Beginning	Ending	Changed from prior report?
RFP:	TBD	TBD	N/A
Design:	Spring 2023 (FY23)	Winter 2024 (FY25)	N/A
Right-of Way:	Winter 2024 (FY25)	Summer 2025(FY26)	N/A
Construction Bidding:	Summer 2026 (FY27)	Fall 2026 (FY27)	N/A
Construction:	Fall 2026 (FY27)	Spring 2028 (FY28)	Yes

Budget:


\$25,100,467

**Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates**

Route 123 & Old Bridge Road Intersection Improvement

Project #20C17013

*** Federal and Local Funding
Occoquan Magisterial District**

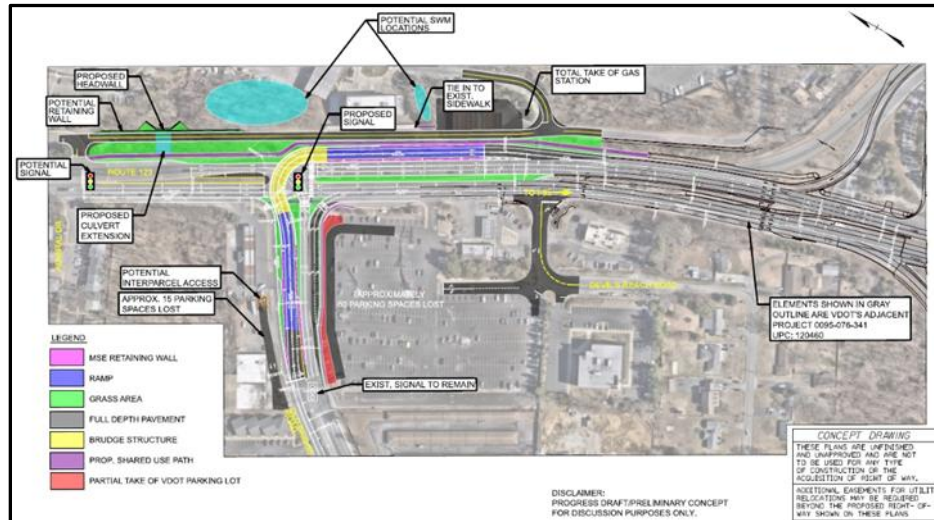

Updates:

- Meetings with VDOT Subject Matter Experts on revised conceptual design are ongoing. VDOT concurrence on the conceptual design is needed before a traffic analysis can begin.

Issues:

- Addressing VDOT design concerns and feedback. Realignment of the ramp may impact some surrounding businesses.
- **Project is not fully funded.**

Timeline:


	Beginning	Ending	Changed from prior report?
RFP:	TBD	TBD	N/A
Design:	Spring 2025 (FY25)	TBD	N/A
Right-of Way:	TBD	TBD	N/A
Construction Bidding:	TBD	TBD	N/A
Construction:	TBD	TBD	N/A

Budget:

\$15,268,403

**Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates**

**Rollins Ford Road
Project#23C17025
* Federal Funding
Brentsville Magisterial District**

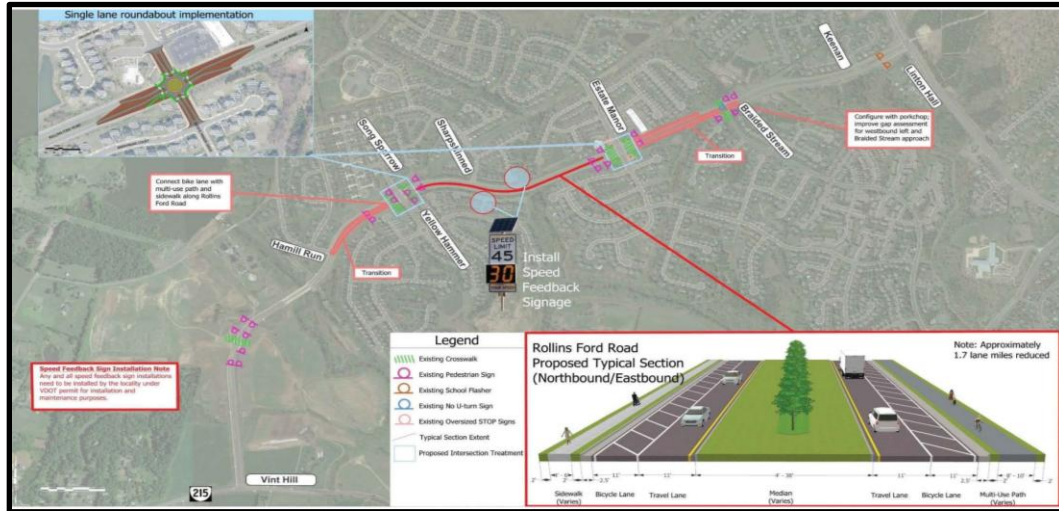

Updates:

- Comments received at the design public hearing were posted on DTCC's website. An item prepared requesting endorsement of the final design is scheduled to go before the BOCS on June 23, 2026.
- **Design activities and Right-of-Way authorization are ongoing.**

Issues:

- None

Timeline:

	Beginning	Ending	Changed from prior report?
Design:	March 2024 (FY24)	Spring 2026 (FY26)	N/A
Right-of Way:	Winter 2026 (FY26)	Summer 2026 (FY27)	N/A
Construction Bidding:	Fall 2026 (FY27)	Fall 2026 (FY27)	N/A
Construction:	Fall 2026 (FY27)	Spring 2028 (FY28)	N/A

Budget:


\$9,470,793

**Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates**

Route 234 Business Battlevue Parkway to Godwin Drive Improvements

Project #25C17002

*** State and Local Funding
Coles Magisterial District**

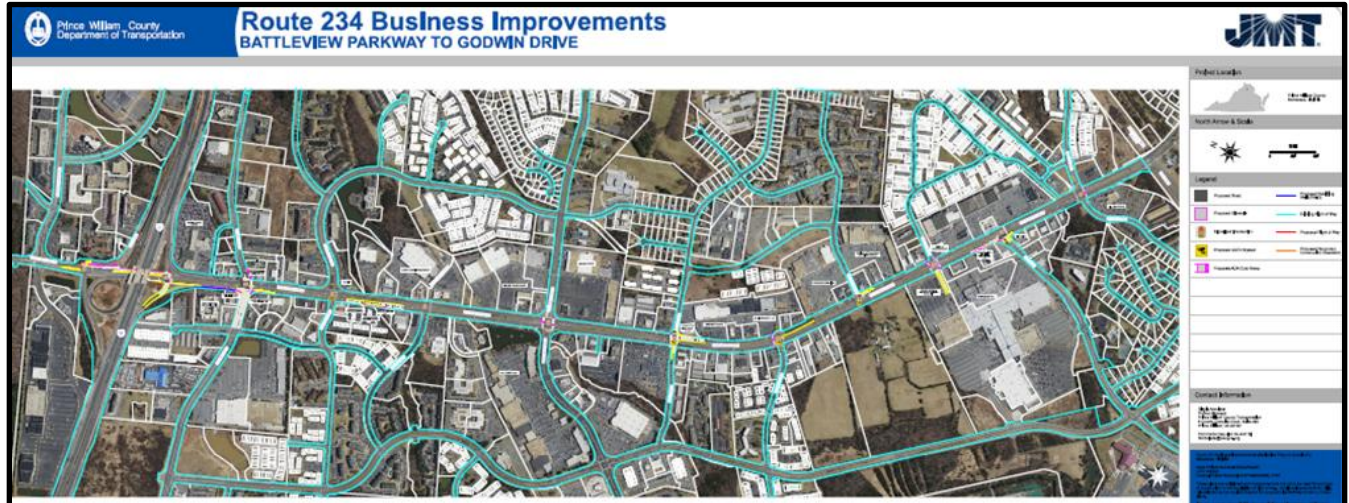

Updates:

- The consultant is finalizing the public hearing plan for resubmission to VDOT.
- The travel demand model, part of the Operational and Safety Analysis Report (OSAR), was submitted to VDOT for review.
- Design activities are ongoing.

Issues:

- The Operational and Safety Analysis Report (OSAR) will take several months to finalize and obtain approval; therefore, it will require an expedited review by VDOT to keep the project moving at a good pace.

Timeline:

	Beginning	Ending	Changed from prior report?
Design:	Winter 2024 (FY25)	Fall 2026 (FY27)	N/A
Right-of Way:	Winter 2026 (FY27)	Fall 2027 (FY28)	N/A
Construction Bidding:	Winter 2027 (FY28)	Winter 2027 (FY28)	N/A
Construction:	Spring 2028 (FY28)	Spring 2030 (FY30)	N/A

Budget:

\$19,758,831


Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates

Route 234 Sudley Manor Drive Interchange

Project #25C17012

*** Regional Funding (PPTA Unsolicited NVTAFunding)**

Brentsville Magisterial District

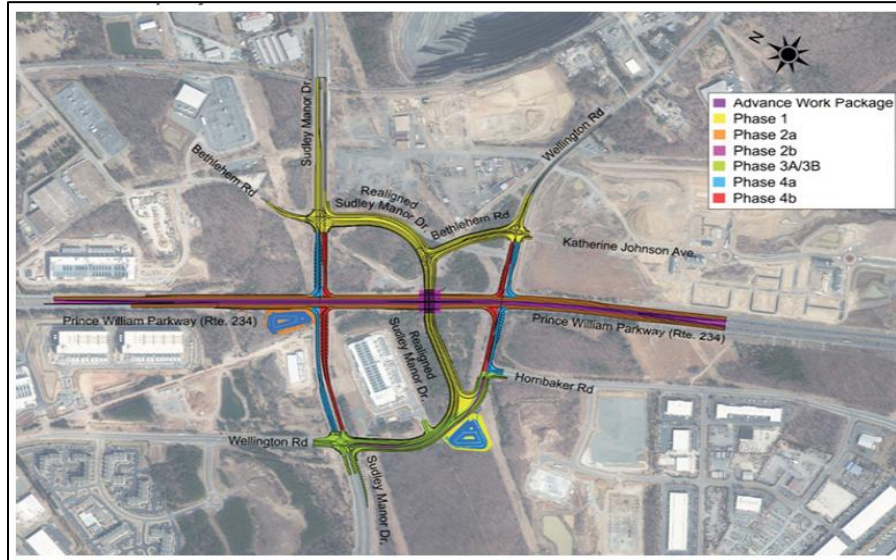

Updates:

- A Public Information Meeting is scheduled for October 7, 2026.
- **Scope validation period is ongoing.**
- **Design criteria approval is ongoing.**

Issues:

- None

Timeline:


	Beginning	Ending	Changed from prior report?
Design:	Spring 2025 (FY25)	TBD	N/A
Right-of Way:	TBD	TBD	N/A
Design-Build RFDP Issuance	Winter 2026 (FY26)	Summer 2026 (FY27)	N/A
Design/Build Contract	July 2026 (FY27)	December 2030 (FY31)	Yes

Budget:

\$119,700,000

**Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates**

**North Woodbridge Pedestrian Bridge
Project #23C17024
* Federal Funding
Woodbridge Magisterial District**

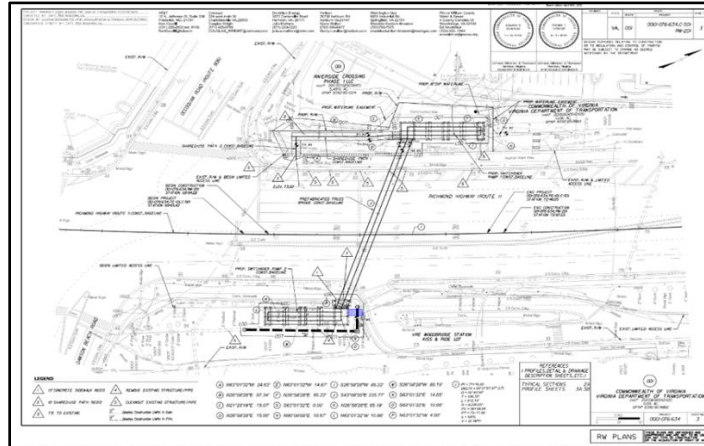

Updates:

- The Invitation for Bid was advertised on August 24, 2026.
- Bids will open on September 24, 2026.
- The revised Appendix A was approved by the Board on September 1, 2026.
- The maintenance agreement between PWC and VDOT is scheduled to go before the Board for approval on September 22, 2026. Coordination with FFM is ongoing to ensure funding will be available in the future to support the identified PWC maintenance needs.

Issues:

- Securing additional funding.

Timeline:


	Beginning	Ending	Changed from prior report?
Design:	June 2025 (FY25)	August 2026 (FY27)	Yes
Right-of Way:	April 2026 (FY26)	July 2026 (FY27)	Yes
Construction Bidding:	August 2026 (FY27)	September 2026 (FY27)	Yes
Construction:	November 2026 (FY27)	November 2028 (FY29)	Yes

Budget:

\$8,548,063

**Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates**

**Graduation Drive Parking Lot
Project #25C17010
*Local Funding
Gainesville Magisterial District**

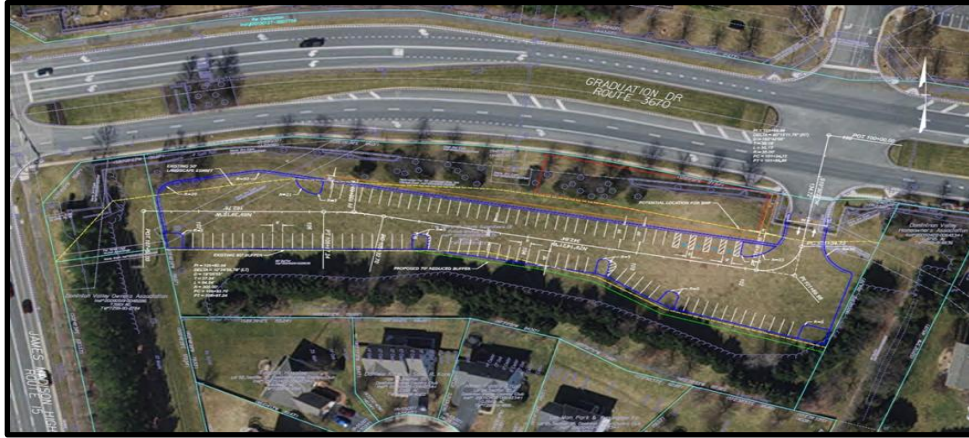

Updates:

- Signal warrant analysis and crosswalk study reports were completed by the consultant.
- This parking lot, including the stormwater management pond, will need to be maintained by the County. Maintenance coordination is ongoing with FFM.
- **The consultant submitted a 30% plan exhibit in April 2026. Currently, the Consultant is advancing plans for a 60% full plan set to be submitted in October 2026.**

Issues:

- None

Timeline:

	Beginning	Ending	Changed from prior report?
Design:	April 2025 (FY25)	December 2027 (FY28)	N/A
Right-of-Way:	January 2027 (FY28)	December 2027 (FY28)	N/A
Construction Bidding:	February 2028 (FY28)	April 2028 (FY28)	N/A
Construction:	May 2028 (FY28)	September 2028 (FY29)	N/A

Budget:


\$1,928,854

**Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates**

**Removal of MOT for Prince William Parkway at Minnieville Road Interchange with
Share Use Path Improvements to Elm Farm Road**

Project 25C17021

***Federal, State, and Regional Funding
Neabsco Magisterial District**

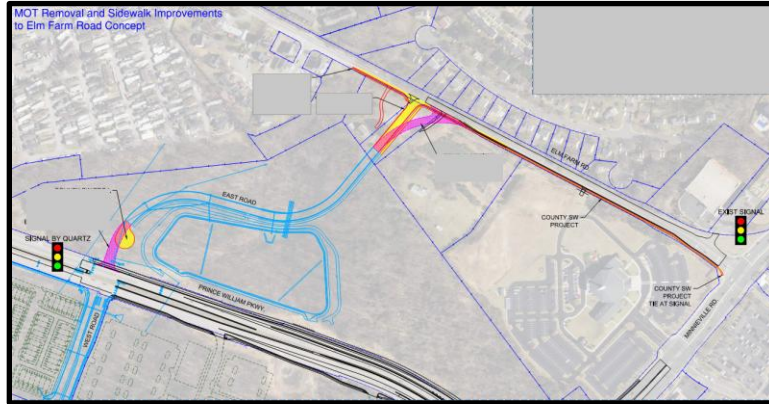

Updates:

- Project survey is planned to begin in September 2026. Survey completion is dependent on the construction of the East MOT road by the Quartz Developer.
- **Coordination with the Interchange and Quartz developers is ongoing.**

Issues:

- None

Timeline:


	Beginning	Ending	Changed from prior report?
Design:	August 2026 (FY27)	August 2028 (FY29)	N/A
Right-of-Way:	Fall 2026 (FY27)	Winter 2027 (FY28)	N/A
Construction Bidding:	Summer 2028 (FY29)	Fall 2028 (FY29)	N/A
Construction:	TBD	TBD	N/A

Budget:

\$10,786,860

**Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates**

**Route 1 Widening (Cardinal Drive to Route 234) Study
Project 25C17011
*Local Funding
Potomac and Woodbridge Magisterial Districts**

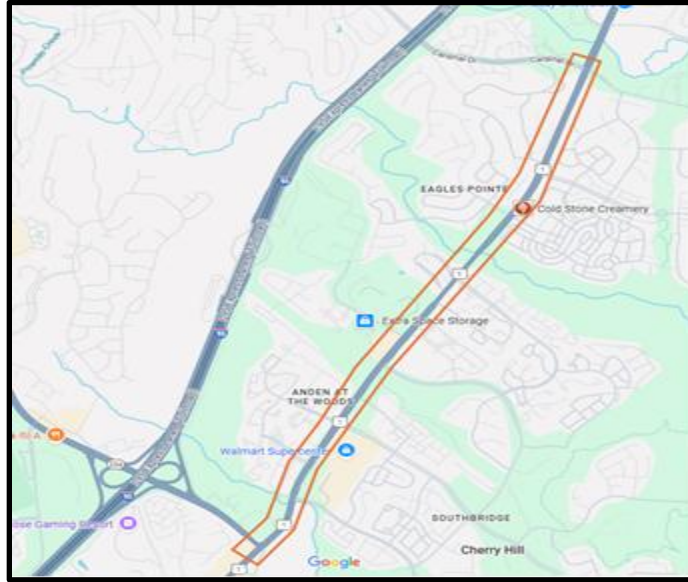

Updates:

- DTCC received final VDOT comments for the shorter phase of the project in June 2026. VDOT's comments were incorporated into the plan and have been approved.
- **An application for Smart Scale funding is complete.**

Timeline:

	Beginning	Ending	Changed from prior report?
Study Timeline	May 2025 (FY25)	June 2026 (FY26)	N/A

Budget:

\$500,000

Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates

Bicycle and Pedestrian Improvements Projects

Sudley Manor Drive Sidewalk- Linton Hall Road to Victory Lakes Loop Project: 23C17010

Updates:

- **Construction of the sidewalk is complete.**
- **Guardrail installation will be initiated shortly.**
- **Project is scheduled for completion in October 2026.**

Status: Construction activities are ongoing.

Budget: \$1,510,598 (federal and local funding)

Brentsville Magisterial District

Ellicott Street Sidewalk- Occoquan Greenway Connect Project: 23C17013

Updates:

- **Verizon and Comcast submitted the cost estimates and design for relocations/adjustments of their facilities.**
- **The request for Right-of-Way Authorization was submitted to VDOT on August 21, 2026.**

Status: Design activities are ongoing.

Budget: \$2,887,821.51 (federal and local funding)

Occoquan Magisterial District

Horner Road Park and Ride Lot Expansion Project: 22C17006

Updates:

- **Project completion is anticipated in fall 2026.**

Status: Construction activities are ongoing.

Budget: \$2,800,000 (Northern Virginia Transportation Commission funding)

Occoquan Magisterial District

**Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates**

Token Forest Sidewalk Project: 23C17014

Updates:

- **The project was accepted by VDOT.**
- **This will be the last report for this project.**

Status: Completed

Budget: \$849,452 (federal and local funding)

Occoquan Magisterial District

Prince William Parkway Sidewalk (Northside of Prince William Parkway Summerland Drive to the Horner Road Commuter Lot) Project: 23C17017

Updates:

- **Bids opened on August 6, 2026.**
- **Three bids were received from A&M Concrete Corp, M&F Concrete, Inc. and Sagres Construction Corp.**
- **M&F Concrete, Inc. was the lowest bidder for \$1,686,088.88. The contract award and Notice to Proceed are pending.**

Status: Construction to begin soon.

Budget: \$5,797,415 (Federal funding)

Woodbridge Magisterial District

Old Carolina Road Shared Use Path (Walter Robinson Lane to Heathcote Boulevard) Project: 23C17019

Updates:

- **Coordination with all involved utility owners for relocation/adjustments of their facilities is ongoing.**
- **Right-of-Way and easement acquisition activities are in progress.**
- **The final plan was submitted to the Town of Haymarket on August 13, 2026.**
- **VDOT, PWC Department of Development Services, PWC Department of Public Works Environmental Services and Prince William Water comments received on August 13, 2026 are being addressed.**

Status: Design and Right of Way activities are ongoing.

Budget: \$1,852,235 (federal and local funding)

Gainesville Magisterial District

Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates

Graham Park Road Sidewalk Project: 25C17003

Updates:

- **Coordination with all involved utility owners for relocation/ adjustments of their facilities is ongoing.**
- **PWC Public Works completed the video inspections of the existing storm drain system on August 20, 2026, and the file was submitted to the consultant AMT.**
- **All VDOT comments received on June 3, 2026 are being addressed.**
- **The documentation requesting Public Involvement Approval was submitted to VDOT on August 26, 2026.**

Status: Design activities are ongoing.

Budget: \$4,597,158 (federal, regional, and local funding)

Potomac Magisterial District

Lions Field Road Sidewalk Project: 25C17004

Updates:

- Test pits for utility companies are planned.
- **Right-of-Way authorization is in progress.**

Status: Design activities are ongoing.

Budget: \$4,930,049 (federal, regional, and local funding)

Potomac Magisterial District

Colchester Road Sidewalk Improvement Project: 25C17005

Updates:

- **Right-of-Way acquisition is in progress. One parcel was cleared, and two parcels will go before the Board for a Certificate of Take in September 2026.**

Status: PE phase has begun.

Budget: \$3,366,839 (federal and local funding)

Woodbridge Magisterial District

Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates

Jefferson Park/Veterans Park Connector Trail Project: 25C17018

Updates:

- **DMY completed geotechnical subsurface explorations in the field on August 21, 2026.**
- **DMY is working on the lab testing analysis and completion of the Geotechnical Engineering Report.**
- **Prefabricated pedestrian bridge to be ordered via a Fairfax County contract.**
- **Anticipate the project to be completed by Public Works in early 2027.**

Status: Design activities are ongoing.

Budget: \$985,000 (local funding)

Woodbridge Magisterial District

Route 15 Trail at Catharpin Creek: 25C17014

Updates:

- **The project is currently on hold.**

Status: Project is on hold.

Budget: \$2,967,714 (Local funding)

Gainesville Magisterial District

Beau Ridge Drive Sidewalk Project: 25C17020

Updates:

- Design package review is in progress. Review comments were received from VDOT and PWC Development Services. Comments are being addressed.
- **Property notification letters regarding test hole activities were sent to impacted property owners.**

Status: Design activities are ongoing.

Budget: \$850,000 (Local funding)

Potomac Magisterial District

Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates

Shenandoah Park Improvements Project: 26C17011

Updates:

- **Survey and utility designation activities were completed on July 22, 2026.**
- **Preliminary design is in progress.**
- **Anticipate adding this work to the Parks project for the Shenandoah Horticultural Therapy Center, with an anticipated date of early 2027.**

Status: Design activities are ongoing.

Budget: \$735,000 (local funding)

Coles Magisterial District

**Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates**

Braided Stream Flasher Project Design

Project # 23C17002

***Federal Funding**

Brentsville Magisterial District



Updates:

- **Thirty-day test window with VDOT was initiated on August 31, 2026.**
- **Project is scheduled for completion in October 2026.**

Issues:

- VDOT eventually approved a 120V supply, and the site is now energized.

Timeline:

	Beginning	Ending	Changed from prior report?
Design:	October 2022 (FY23)	January 2023 (FY23)	N/A
Right-of-Way:	N/A	N/A	N/A
Construction Bidding:	Summer 2024 (FY24)	Summer 2024 (FY24)	N/A
Construction:	Fall 2024 (FY25)	Fall 2026 (FY27)	N/A

Budget:

\$366,039

**Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates**

Upcoming Projects

Old Bridge Road Widening (Colby Drive to Minnieville Road) Project: 27C17004

Project Descriptions:

The project will widen approximately 0.4 miles of Old Bridge Road (Route 641) from Colby Drive to Minnieville Road from four to six lanes and will include improvements and signal modifications to the intersection of Old Bridge Road and Minnieville Road to accommodate the additional lanes and further improve operations and will include a shared-use path that will facilitate bicycle and pedestrian access.

Status: Preliminary design

Budget: \$25,000,000 (regional funding)

Occoquan Magisterial District

Route 234 Operational Improvements Project:

Project Descriptions:

The project will design and construct approximately 12 CCTV cameras, two dedicated dynamic message signs, four changeable message signs, detector enhancement, larger cabinet installation, and fiber communication installation, which will improve safety, reliability, operational efficiency, and mobility for travelers.

Status: Preliminary design

Budget: \$10,000,000 (regional funding)

Brentsville, Coles, Gainesville, Occoquan, and Potomac Magisterial Districts

**Triangle Mobility Hub and First/Last Mile Connection Improvements Project:
27C17003**

Project Descriptions:

The project will design and construct a mobility hub to support new OmniRide bus routes and future high-capacity transit along the Route 1 corridor. It also includes a 200-foot pull-off area that can accommodate up to three 45-foot passenger buses simultaneously, bus shelters, lighting, and transit amenities including bike racks and lockers.

Status: Preliminary design

Budget: \$10,000,000 (regional funding)

Potomac Magisterial District

Department of Transportation and Capital Construction (DTCC)
Capital Improvement Project Updates

Maintenance of Effort (MOE) Update

In order for the County to receive its annual allocation of Northern Virginia Transportation Authority (NVTA) 30% local funds, the County is required to expend \$25,798,543 (by the end of the fiscal year) in local funds on transportation projects. Below is the total amount of local funds used on CIP transportation projects YTD. FY25 certification was accepted by NVTA.

<u>FY27 Total</u>	<u>\$6,758,636.33</u>
--------------------------	------------------------------
